


# QUALITY CONTROL AND QUALITY ASSURANCE



ICS is able to expertly witness, perform and develop a variety of testing procedures in coordination with reputable testing agencies, including but not limited to performance testing, impact resistance testing, adhesion and compatibility testing.

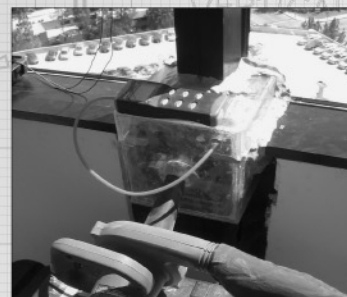

We also perform shop and field inspections to confirm compliance to the design and contract documents. In addition ICS is also called upon to perform due diligence forensics on existing buildings.

ICS prepares comprehensive reports with recommendations for repair, if any required, that are of great value for buyers, sellers and property managers that require a comprehensive assessment.

ICS can assist in the preparation and evaluation of quality control procedures which should be adhered to during shop manufacturing and field installation to ensure that critical waterproofing sealants, gaskets, metal joinery, flashings and connections are installed per the contract documents.

Testing, Inspection and Quality Control are worthwhile investments in the future of a trouble free building.

## ICS QA/QC CHECKLIST



Fabrication Department

### QUALITY CONTROL INSPECTION

Project Name:	Date Inspected:
Job Number:	Lot Number:
Order Number:	Job Description:
Sheet Number:	QC Sheet Number:
Drawing Number:	Tolerance:

QUALITY CHECK POINTS	ACCEPT (I)	REJECT (O)	REMARKS
1 Material Specification			
2 Dimensions Length, Width, Height, Spacing, etc.			
3 Bending/Rolling Position Height, Degree, Radius			
4 Machining Operations Diameter, Centering, Tap, Counterbore, etc.			
5 Joint Material Sawtooth, Roll, Welding, Sloves, etc.			
6 Welding Specification Weld, Continuity, Penetration, etc.			
7 Exposed Surface Area Dirt, Scale, Debris, Scratches, etc.			
8 General Design Clearance, Lap, Spacing, etc.			
9 Finish Product Polishing Specification			
10 Special Accessories Supplied, Fabricated, etc.			
11 Initial Testing and Pre-Assembly			

#### NOTES

Total Quantity Ordered:	Dispatched to:	Checked By:
Quantity Inspected:	Manufacturing Plant:	Quality Control:
Quantity Approved:	Plant Department:	
Quantity Rejected:	Project Site:	

1/8" THK. EXTR. ALUM COVER

#10 x 5/8" PH - SCREW

SCREW # 816550
